
ID	Task Name	Duration	Start	Finish
1	**Key Dates**	**805 days**	**Fri 17/05/13**	**Fri 31/07/15**
2	Full Approval Submission	0 days	Fri 17/05/13	Fri 17/05/13
3	Works Start on Site	0 days	Mon 22/07/13	Mon 22/07/13
4	Works Completed	0 days	Fri 31/07/15	Fri 31/07/15
5	Scheme Open	0 days	Fri 31/07/15	Fri 31/07/15
6	**Governance**	**213 days**	**Mon 29/04/13**	**Thu 28/11/13**
7	**Project Board Meetings**	**213 days**	**Mon 29/04/13**	**Thu 28/11/13**
13	**Project Review Meetings**	**154 days**	**Thu 30/05/13**	**Thu 31/10/13**
20	**Delivery Group Meetings**	**154 days**	**Wed 22/05/13**	**Wed 23/10/13**
27	**Communications and Engagement Strategy**	**121 days**	**Mon 01/04/13**	**Tue 30/07/13**
44	**Traffic Regulation Order**	**470 days**	**Fri 01/03/13**	**Fri 13/06/14**
52	**Land Process**	**71 days**	**Mon 22/07/13**	**Tue 01/10/13**
56	**Monitoring and Evaluation**	**2808 days**	**Fri 15/03/13**	**Fri 20/11/20**
57	Monitoring and Evaluation Plan submission	0 days	Fri 15/03/13	Fri 15/03/13
58	**Pre-construction Evaluation**	**152 days**	**Mon 08/04/13**	**Fri 06/09/13**
62	**Scheme Delivery**	**740 days**	**Mon 22/07/13**	**Fri 31/07/15**
64	**Year 1 Post Evaluation**	**124 days**	**Mon 25/07/16**	**Fri 25/11/16**
68	**Year 5 Post Evaluation**	**124 days**	**Mon 20/07/20**	**Fri 20/11/20**
72	**Start of Construction**	0 days	Mon 01/07/13	Mon 01/07/13
73	**Aspley Lane Junction and Widenings**	**171 days**	**Mon 01/07/13**	**Wed 18/12/13**
98	**Crown Island Structures Works**	**315 days**	**Mon 07/10/13**	**Sun 17/08/14**
108	**Hucknall Road Structures Works**	**77 days**	**Mon 07/10/13**	**Sun 22/12/13**
121	**Crown Island Carriageway Works**	**189 days**	**Mon 05/01/15**	**Sun 12/07/15**
153	**Western Boulevard and Valley Road**	**147 days**	**Mon 13/01/14**	**Sun 08/06/14**
158	**Wilkinson Street Junction**	**70 days**	**Mon 09/06/14**	**Sun 17/08/14**
166	**Nottingham Road Junction**	**70 days**	**Mon 18/08/14**	**Sun 26/10/14**
175	**Hucknall Road Junction**	**210 days**	**Mon 20/01/14**	**Sun 17/08/14**
208	**End of Construction**	0 days	Sun 12/07/15	Sun 12/07/15

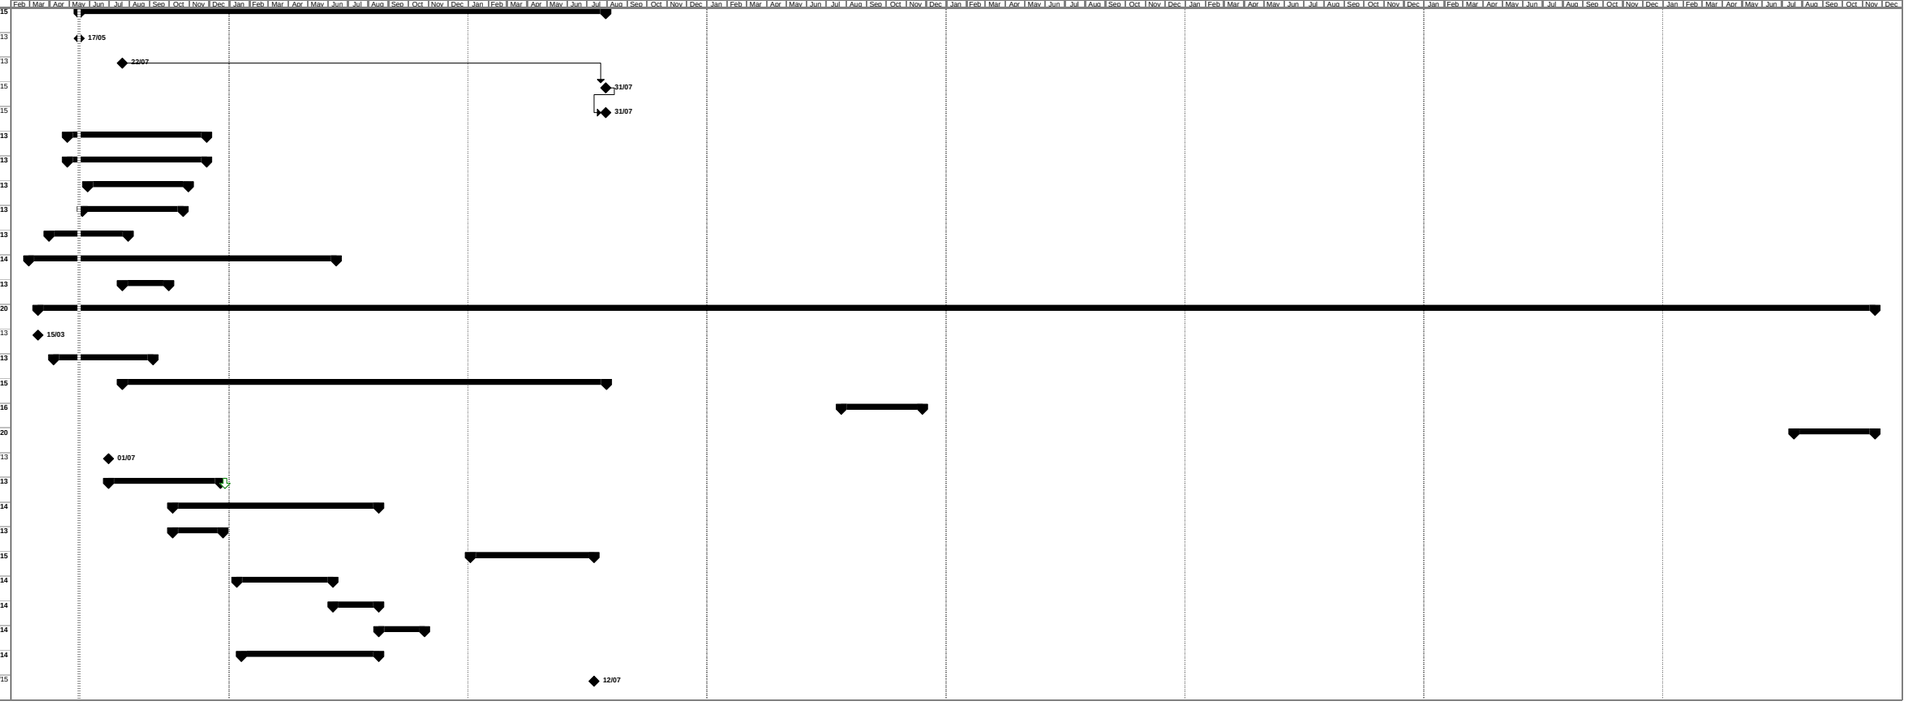

Project: Ring Road Project Plan
Date: May 2013

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External MileTask | Split
